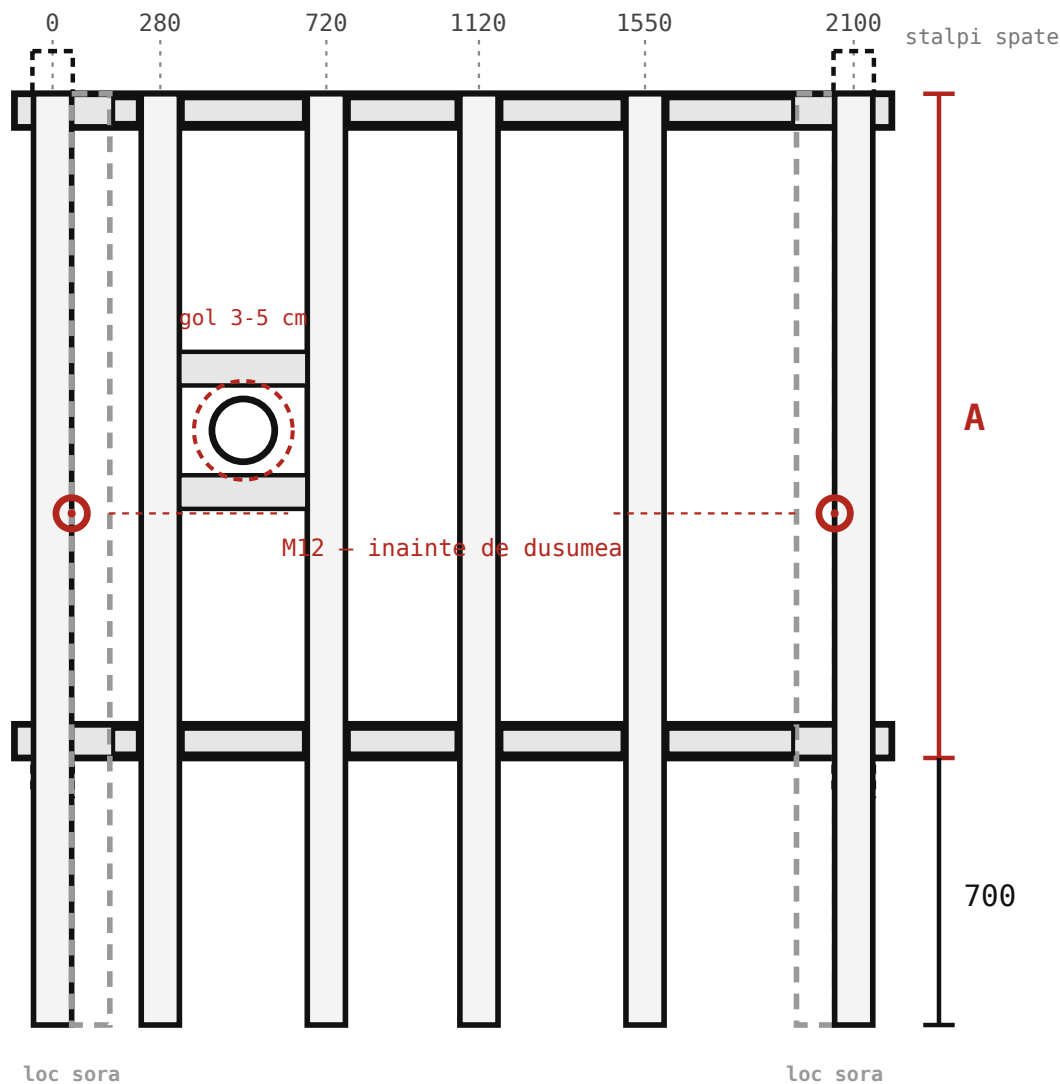


PODEA

6 joiste ACUM · surorile inainte de CASA · 24.07.2026



masoara A inainte sa tai



slotul de langa joistele de capat ramane LIBER – surorile intra acolo inainte de casa


$$\text{JOISTA} = A + 700 \text{ (~2430-2450)}$$

tele la ras cu glulamul spate · toate 6 EGALE (surorile la fel, mai tarziu)

 C2 90x90x65
x12 (stoc 14 – ajunge; +4 la surori)

 HECO 6x100 · T30 · colturi spate
x6

 HECO 6x80 · T30 · coltare+blocaje
x87 pachetul e la limita → +1

 INOX A2 5x60 · T25 · +68 la surori
x204 GSR ambreiaj 8-12 · NU impact

 TIJA M12 + saiba lata + piulita
x2 gaura Ø13

SCULE:

GSR 18V ambreiaj

GDR 18V + T30


HS7611K + impins

ruleta+nivela

PST 700E decupaje

cleme+capre

- capul surubului LA RAS – nici iesit, nici ingropat
- pregaurire 4-5 doar la capetele scandurilor

① 
MASOARA A

② 
TAIE 6 EGALE

③ 
JOISTE + C2

④ 
BLOCAJE + M12

⑤ 
DUSUMEA rost 5
